


ITEM 11

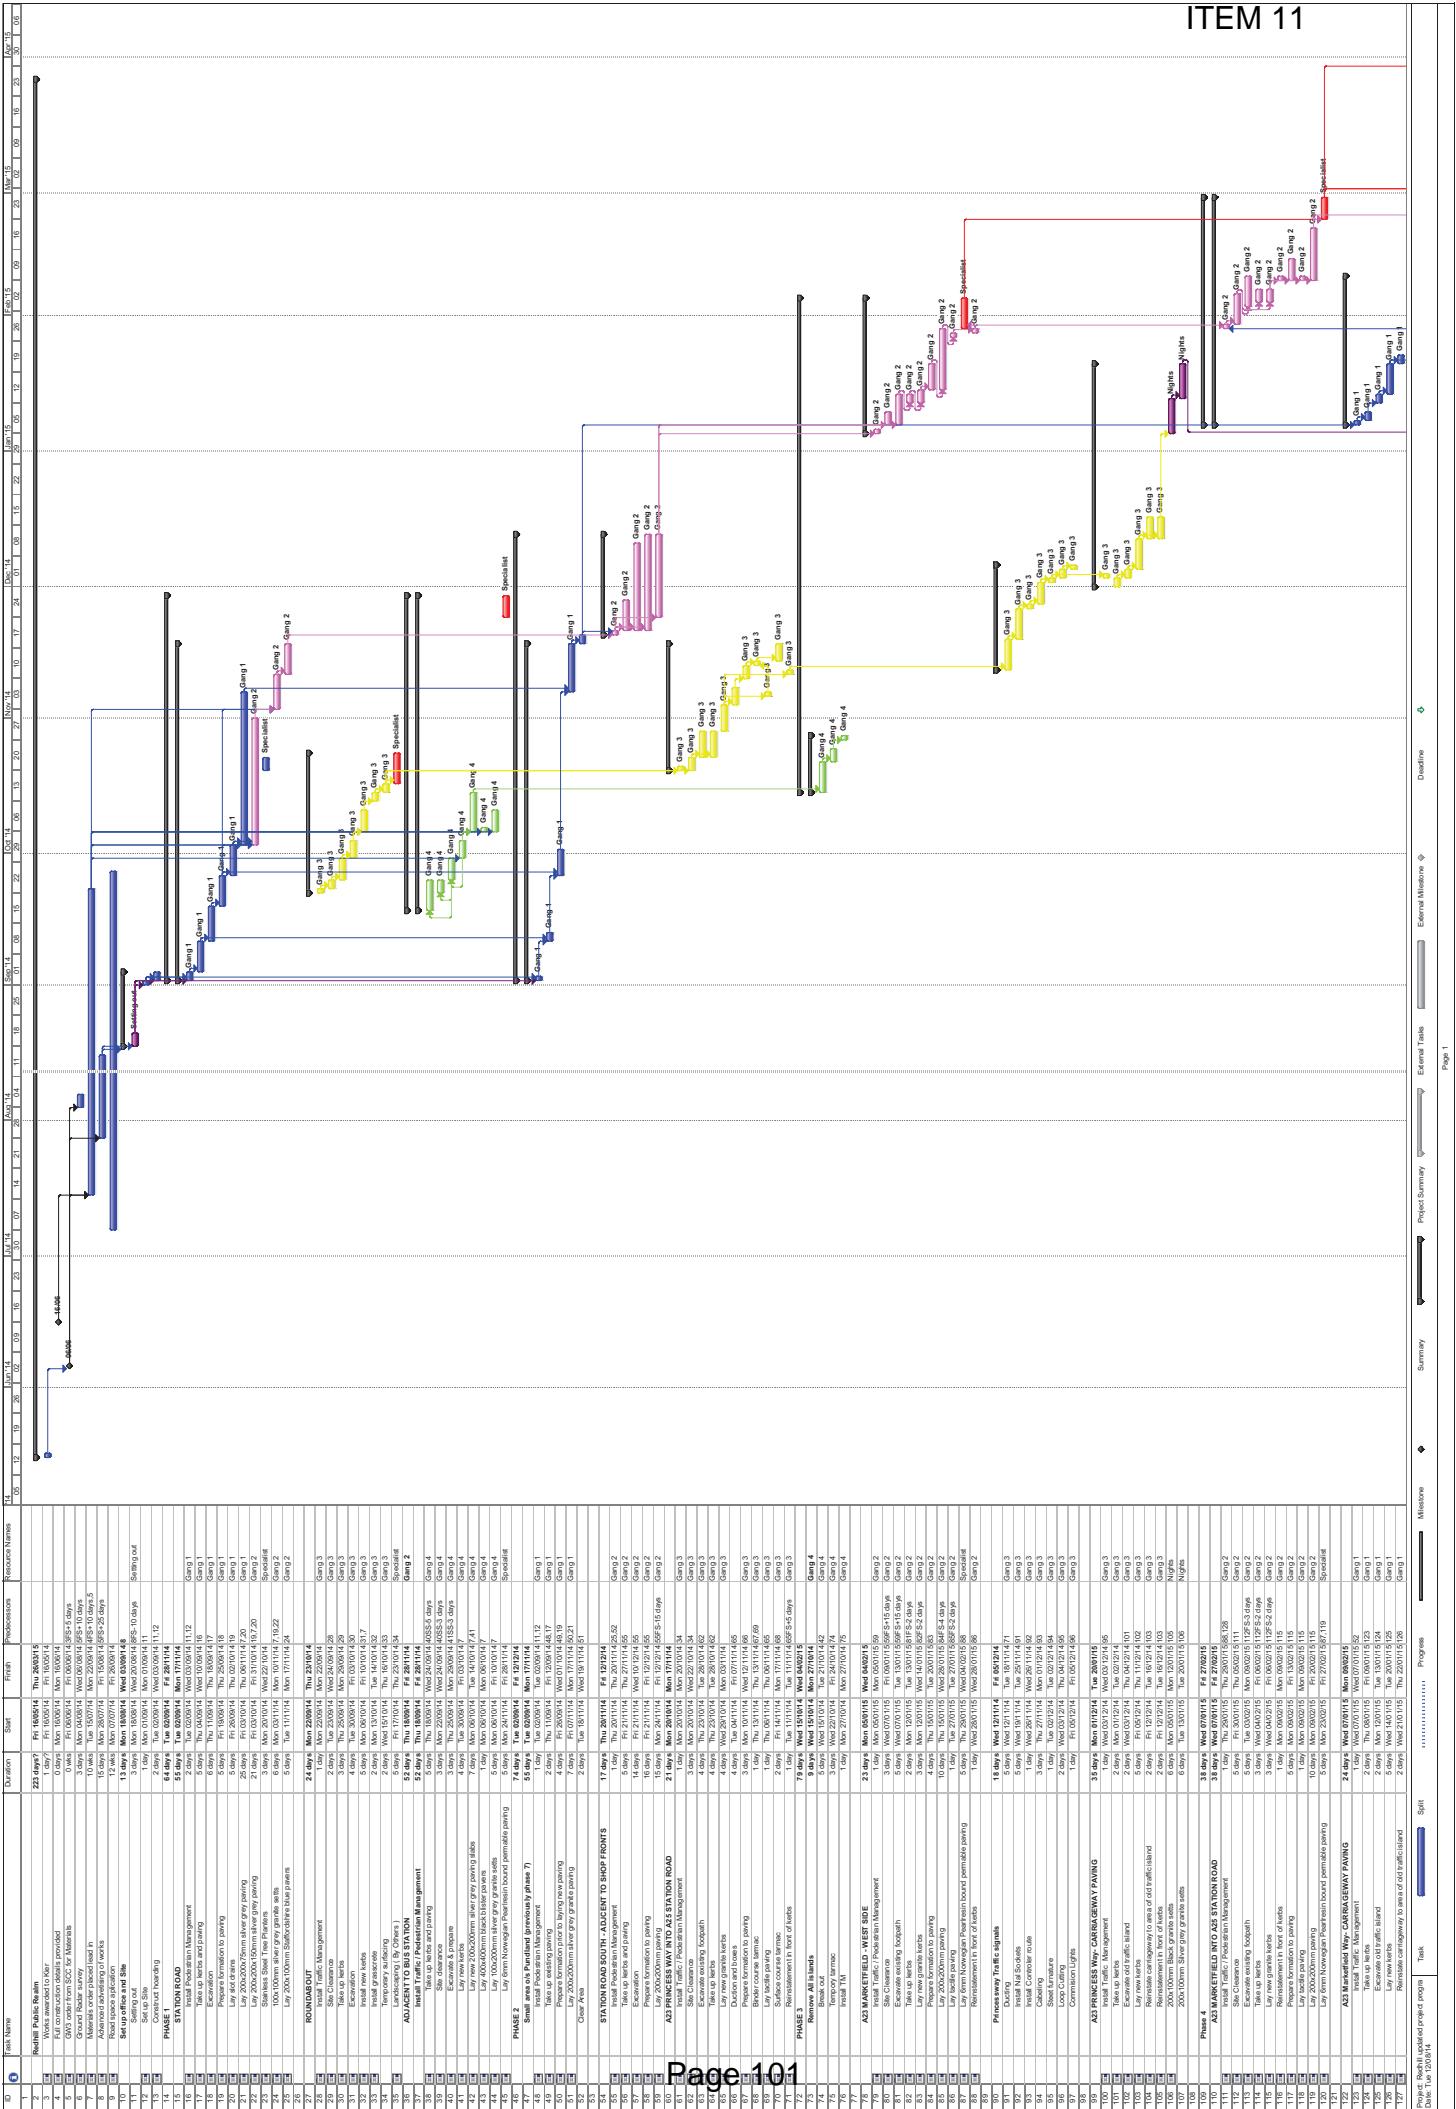

Page 101

Project Summary External Tools Summary Milestone Progress Split

External Metrics

Page 1

Entered Metrics

Page 1

ITEM 11

ID	Task Name	Start Date	Finish Date	Duration	Predecessors	Resource Names
10	Demolition work of walls	2 days	Wed 23/01/15			Gang 1
11	200 x 100mm block & re-sho screeds	6 days	Fri 23/01/15	2 days	Mon 26/01/15	Gang 1
12	Carpenter	6 days	Tue 27/01/15	1 day	Mon 26/01/15	Nigra
13	200 x 100mm block & re-sho screeds	6 days	Thu 29/01/15			Nigra
130	BUS STATION ENTRANCE / PAVED FEATURE	27 days	Wed 07/02/15	1 day	Mon 26/01/15	Gang 3
131	Traffic management	1 day	Wed 07/02/15	1 day	Mon 26/01/15	Gang 3
132	Excavation	1 day	Thu 08/02/15			Gang 3
133	Excavation	1 day	Thu 08/02/15			Gang 3
134	Excavation	1 day	Thu 08/02/15			Gang 3
135	Lay granite kerbs	4 days	Fri 09/02/15	1 day	Mon 26/01/15	Gang 3
136	Lay granite kerbs	4 days	Fri 09/02/15	1 day	Mon 26/01/15	Gang 3
137	200 x 100mm block & re-sho screeds	10 days	Mon 12/02/15	1 day	Thu 12/02/15	Nigra
138	Reinstatement	1 day	Tue 13/02/15			Gang 3
139	Phase 6					
140	Traffic Signal Installation	36 days	Thu 26/01/15	1 day	Mon 26/01/15	Gang 3
141	Drilling	14 days	Thu 26/01/15	1 day	Mon 26/01/15	Gang 3
142	Excavation	5 days	Thu 26/01/15	1 day	Mon 26/01/15	Gang 3
143	Excavation	5 days	Thu 26/01/15	1 day	Mon 26/01/15	Gang 3
144	Excavation	5 days	Thu 26/01/15	1 day	Mon 26/01/15	Gang 3
145	Excavation	3 days	Fri 27/01/15	1 day	Mon 26/01/15	Gang 3
146	Spot drainage	1 day	Mon 26/01/15	1 day	Thu 26/01/15	Gang 3
147	Drilling	2 days	Mon 26/01/15	1 day	Thu 26/01/15	Gang 3
148	Excavation	1 day	Mon 26/01/15	1 day	Thu 26/01/15	Gang 3
149	ABR STABILISATION	16 days	Thu 26/01/15	1 day	Mon 26/01/15	Gang 3
150	Paved Feature	14 days	Thu 26/01/15	1 day	Mon 26/01/15	Gang 3
151	Resurfacing / Traffic Management	1 day	Thu 26/01/15	1 day	Mon 26/01/15	Gang 3
152	Resurfacing / Traffic Management	5 days	Mon 30/01/15	1 day	Thu 26/01/15	Gang 3
153	Lay new granite kerbs	5 days	Mon 30/01/15	1 day	Thu 26/01/15	Gang 3
154	200 x 100mm block & re-sho screeds	7 days	Mon 30/01/15	1 day	Thu 26/01/15	Nigra
155	Phase 6					
156	ENTRANCE TO STATION GATE	44 days	Mon 26/01/15	1 day	Thu 26/01/15	Gang 3
157	Demolition	3 days	Mon 26/01/15	1 day	Thu 26/01/15	Gang 1
158	Excavation	4 days	Tue 27/01/15	1 day	Mon 26/01/15	Gang 1
159	Excavation	2 days	Tue 27/01/15	1 day	Mon 26/01/15	Gang 1
160	Excavation	2 days	Tue 27/01/15	1 day	Mon 26/01/15	Gang 1
161	Excavation	6 days	Wed 28/01/15	1 day	Mon 26/01/15	Gang 1
162	Excavation	7 days	Wed 28/01/15	1 day	Mon 26/01/15	Specialist
163	Excavation	7 days	Wed 28/01/15	1 day	Mon 26/01/15	Gang 1
164	Excavation	2 days	Thu 29/01/15	1 day	Mon 26/01/15	Gang 1
165	Excavation	10 days	Fri 30/01/15	1 day	Mon 26/01/15	Gang 1
166	Excavation	2 days	Fri 30/01/15	1 day	Mon 26/01/15	Gang 1
167	Excavation	2 days	Fri 30/01/15	1 day	Mon 26/01/15	Gang 1
168	Excavation	15 days	Fri 30/01/15	1 day	Mon 26/01/15	Gang 1
169	Excavation	2 days	Fri 30/01/15	1 day	Mon 26/01/15	Gang 1
170	Block paving & block granite sets	170 days	Mon 03/02/15	1 day	Thu 26/01/15	Gang 2
171	5 x block paving works to various areas (when required)	170 days	Mon 03/02/15	1 day	Thu 26/01/15	Gang 2
172	Phase 6	167 days	Mon 03/02/15	1 day	Thu 26/01/15	Gang 2
173	Carriageway Surfacing	8 days	Mon 03/02/15	1 day	Thu 26/01/15	Mariela
174	Roughsurf	8 days	Mon 03/02/15	1 day	Thu 26/01/15	Mariela
175	Living	10 days	Tue 04/02/15	1 day	Mon 03/02/15	Mariela
176	Demolition	1 day	Tue 04/02/15	1 day	Mon 03/02/15	Mariela
177	Recovery Wdwn's old Q	1 day	Mon 03/02/15	1 day	Mon 03/02/15	Gang 2
178	Recovery Wdwn's new Q	1 day	Tue 05/02/15	1 day	Mon 03/02/15	Gang 2
